



**Northumbria
University**
NEWCASTLE

2025

PROJECT PROPOSAL:

NORTHUMBRIA POST-GRADUATION MUSIC CONCERT



PROJECT TEAM

Our group is appointed as a **Project Analyst**, assessing the progress of the **Northumbria University Concert Project**.

Name	ID	Task	MARKS (%)
DALIA ALIJANDRA GUEVARA HERNANDEZ	25028102	Data analyst, dashboard	16,67
MINH THY LE	25023396	Data analyst, dashboard	16,67
PHAN NGUYET ANH DO	25037050	Problem statement, Beneficiaries, Objectives, Root identification, SPI&CPI	16,67
HA CHI LE	25050734	Conceptual Model, Rich Picture, CATWOE, SPI&CPI	16,67
HUU DUY NGUYEN	25045434	Risk evaluation, Recommendation, presentation design.	16,67
KÊISI CECA	24045693	Stakeholders, Gantt-Chart	16,67



Sprint 1: Discussing

Discussion about project approach

10 Nov - 18 Nov5/5

HN D DA HL J K K

Introduction

• Provide what project they are doing

• Give some details, when it started, and who are the project owners

• What are the key benefits of the project, and who are the beneficiaries

• Students will use the SSM stages to analyse the problem of the selected project

Introduction & Problem Identification

11 Nov - 12 Nov0/12

DA

Project deliverables

13 Nov - 14 Nov

DA

Project benefits and objectives

14 Nov - 15 Nov

DA

Root identification

16 Nov - 17 Nov

DA

Sprint 2: Planning & Execution

Rich picture

18 Nov - 19 Nov1HL

CATWOE

19 Nov - 20 NovHL

Conceptual model

21 Nov - 23 Nov1HL

Stakeholders identification & Analysis

23 Nov - 25 NovK

Sprint 3 Execution

Gantt Chart

26 Nov - 30 NovK

Data Collection

26 Nov - 28 NovJ D

Dashboard Overview

KPI Cards: % On Time, Cost Variance, Planned vs Actual Spend, Days to Ceremony, Over Budget Count

Charts:

- Planned vs Actual Spend by Month (Bar)
- Task Status by Band (Pie)
- Cost Variance by Task (Bar)

Insights:

- 54% tasks on time → room for improvement
- Negative cost variance → £24K over budget
- Catering & Invitations biggest cost overruns

Creating Dashboard

26 Nov - 3 DecJ D

CRITICAL ANALYSIS

Key Metrics from the Dashboard

- Ticket Allocation vs. Usage:** Most faculties show over 90% usage, but Arts has a slightly lower utilisation rate.
- Fraud Estimation:** Law and Health Sciences recorded the highest suspected fraud cases (3 each), followed by Business (6), Engineering (3), and Arts (2).
- Unused Tickets:** Small volumes across all faculties, with most reallocated successfully before the event.
- Waitlist Management:** High fulfilment rates for extra ticket requests, ensuring fairness in allocation.
- Stakeholder Segmentation:** Students, family members, VIPs, staff, and accessibility guests.
- Risk Links:**
 - Risk 4 (Data ticket duplication) aligns with the fraud screening recommendation.
 - Risk 7 (System downtime) addressed via stress testing suggested.

Recommendations:

- Proactive Fraud Checks** – Verify tickets before event day to minimise entry delays.
- Targeted Communication** – Address lower usage in faculties like Arts with clearer reminders and deadlines.
- Automation** – Fully integrate waitlist reallocation to reduce manual processing times.

Evaluation

- Operational Strengths:**
 - High ticket utilisation rates show efficient allocation processes.
 - Fraud detection tracking ensures potential misuse is identified early.
 - Reallocation of unused tickets reduced wasted capacity.
- Areas for Improvement:**
 - Fraud detection is still reactive, happening mainly at scanning points.
 - Faculty-level discrepancies (e.g., Arts) in ticket usage suggest uneven communication or demand.
 - Manual steps remain in place for waitlist processing, creating small delays.

Dashboard evaluation

3 Dec - 4 DecJ D

SPI & CPI analysis

4 Dec - 5 DecDA HL

Sprint 4 Wrap up

Risk evaluation

5 Dec - 7 DecHN

Recommendation and Conclusion

4 Dec - 7 DecHN D J

Presentation design

4 Dec - 8 DecHN

Reference list

8 Dec0/2HL DA

Presentation practice & submission

48 Dec - 9 Dec0/1

HN D DA HL J K K



INTRODUCTION



Project title:

POST-GRADUATION MUSIC CONCERT



Project owner/sponsor:

Northumbria University, London



16 weeks

Start

01/09/2025



End

09/12/2025

20/12/2025

KEY BENEFICIARIES

INSTITUTIONAL VISIBILITY

Improves the **university's public image** through a professionally organised event.



STUDENT ENGAGEMENT

Enhances the overall **student journey** by creating a memorable post-graduation experience.



STRATEGIC INSIGHTS

Produces **valuable operational and behavioural data** that can inform decision-making for future large-scale events.



SOCIAL VALUE CONTRIBUTION

Creates meaningful **social impact** by offering opportunities for volunteering, cultural participation, and collaborative activities.



PROBLEM STATEMENT







ROOT IDENTIFICATION

Northumbria University London has a driven event management system designed to plan and deliver a financially controlled and high-quality concert for **graduating students and associated stakeholders (X)** through the use of data-driven budgeting tools, BI dashboards, cost-monitoring mechanisms, and coordinated decision-making supported by **the project analytics team (Y)** to ensure **efficient use of limited financial resources, improve accountability, enhance student experience, and establish a scalable budgeting model for future university events (Z).**

CONCEPTUAL MODEL

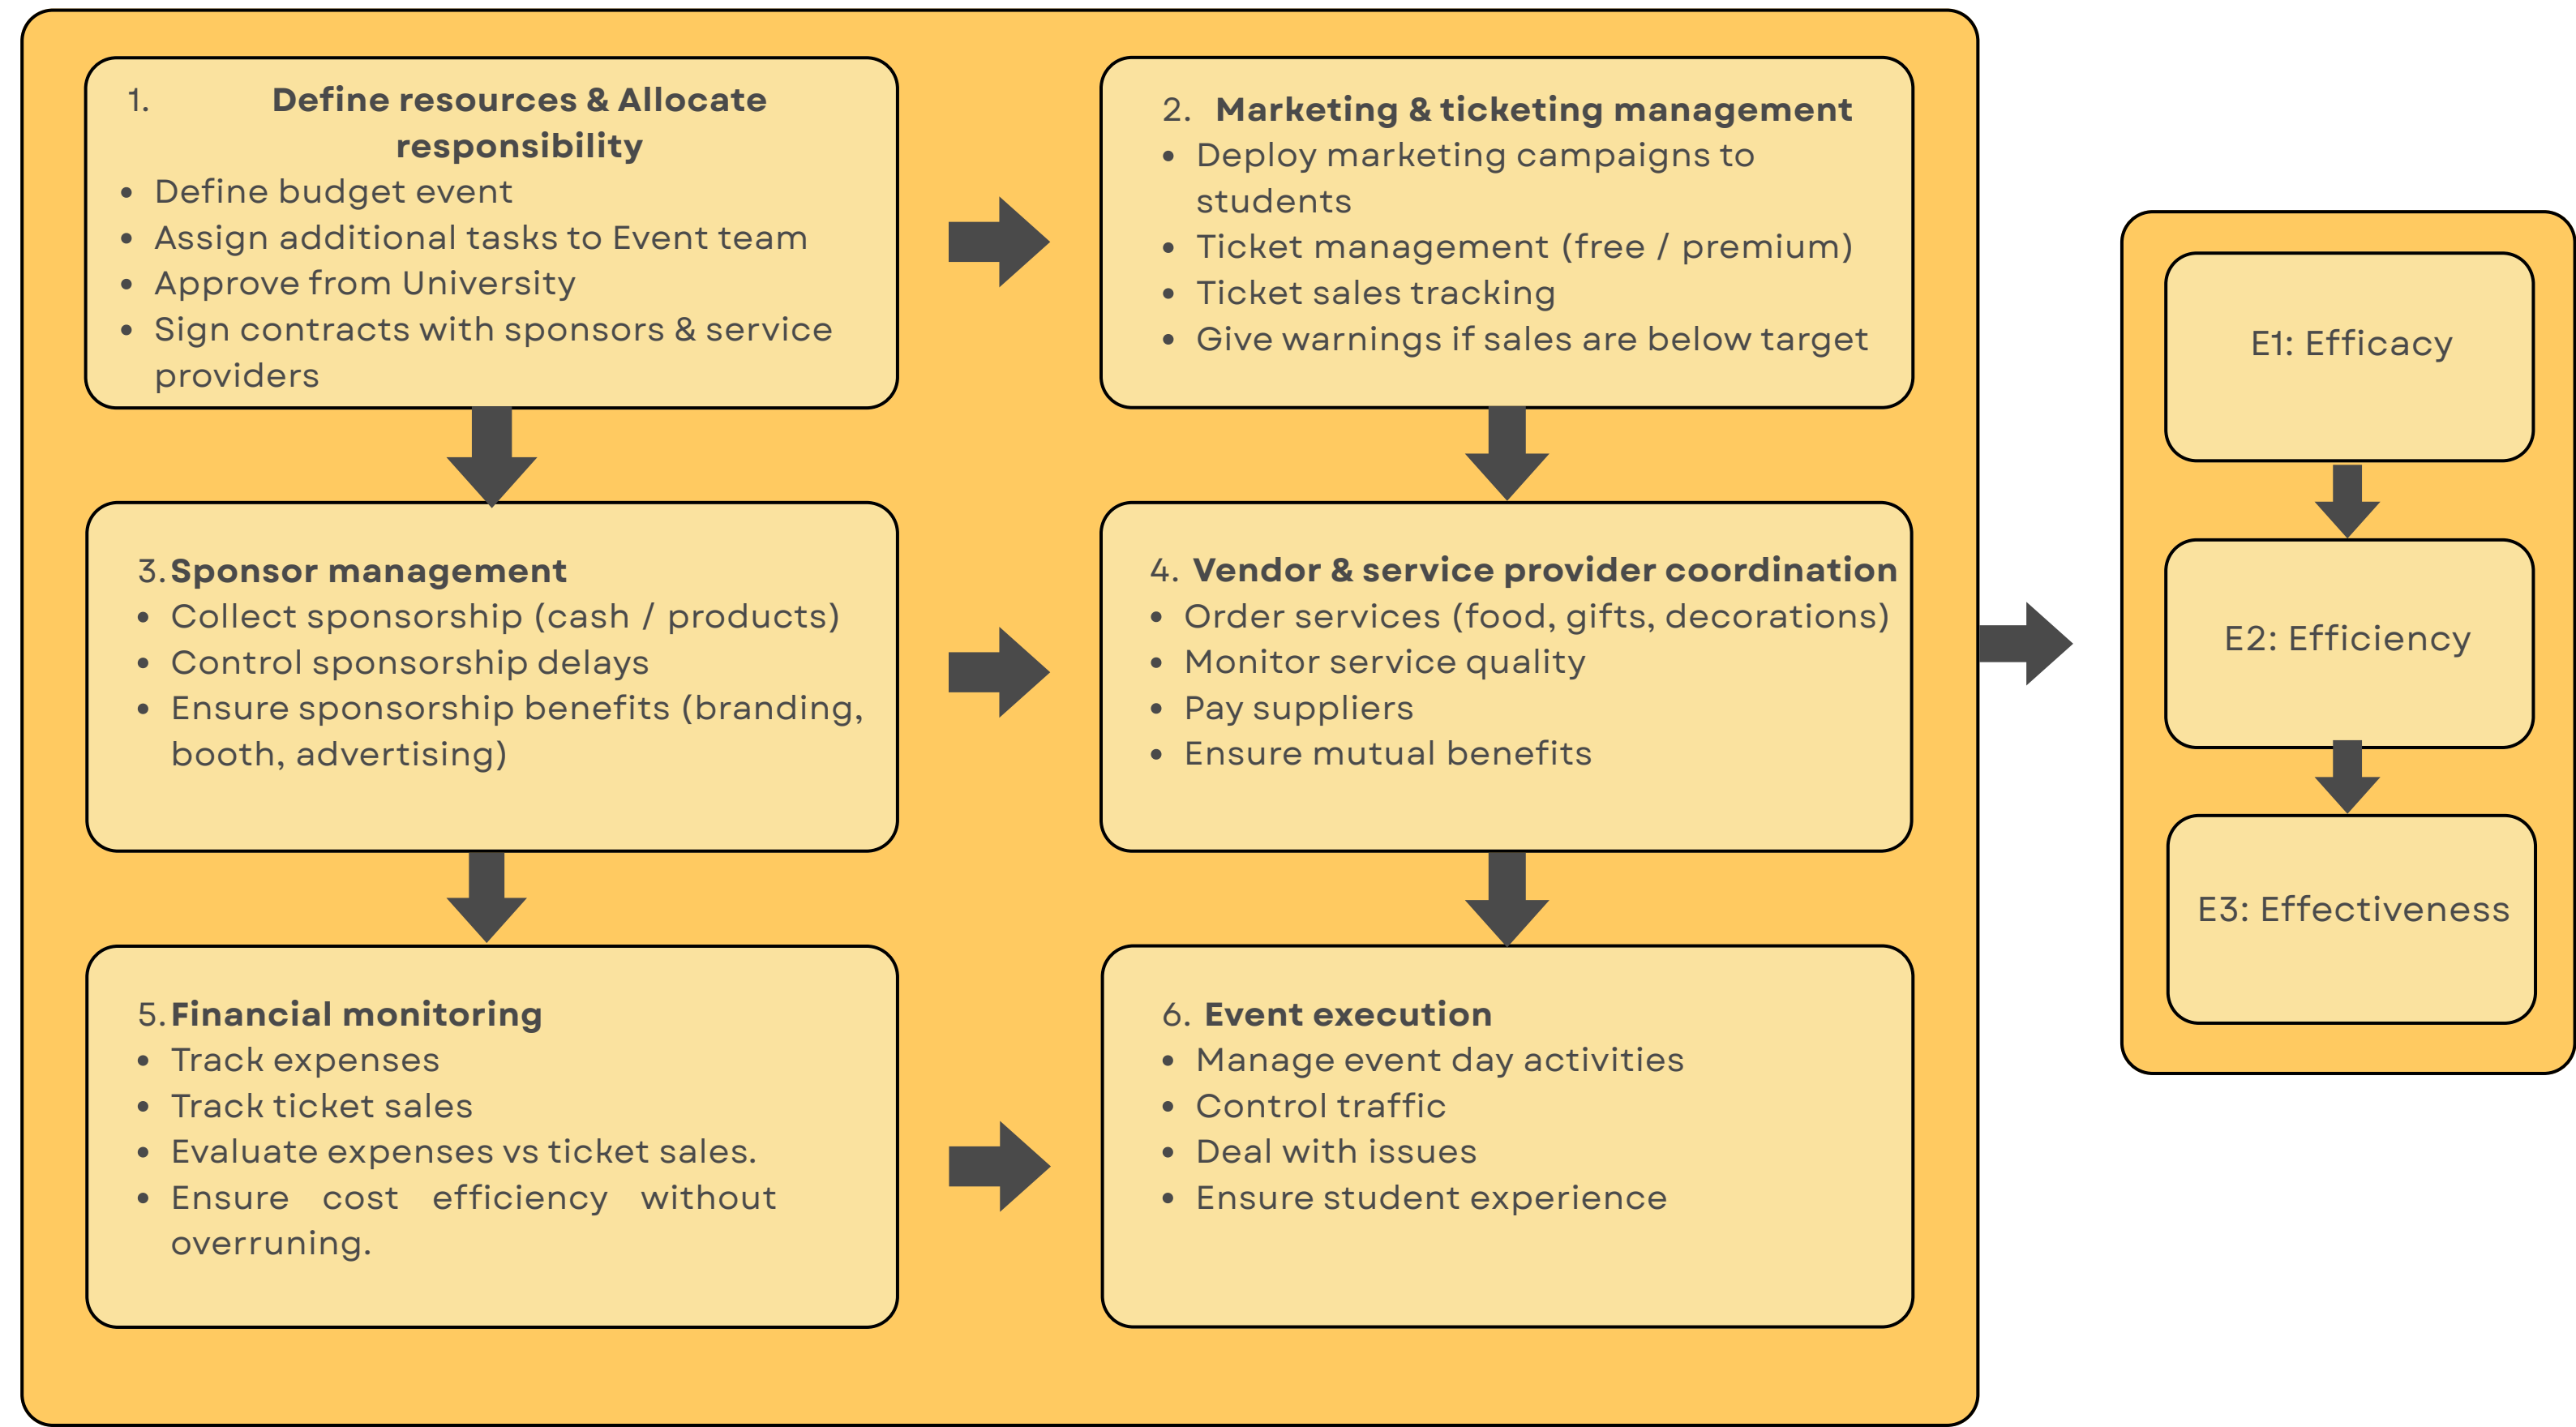

RICH PICTURE

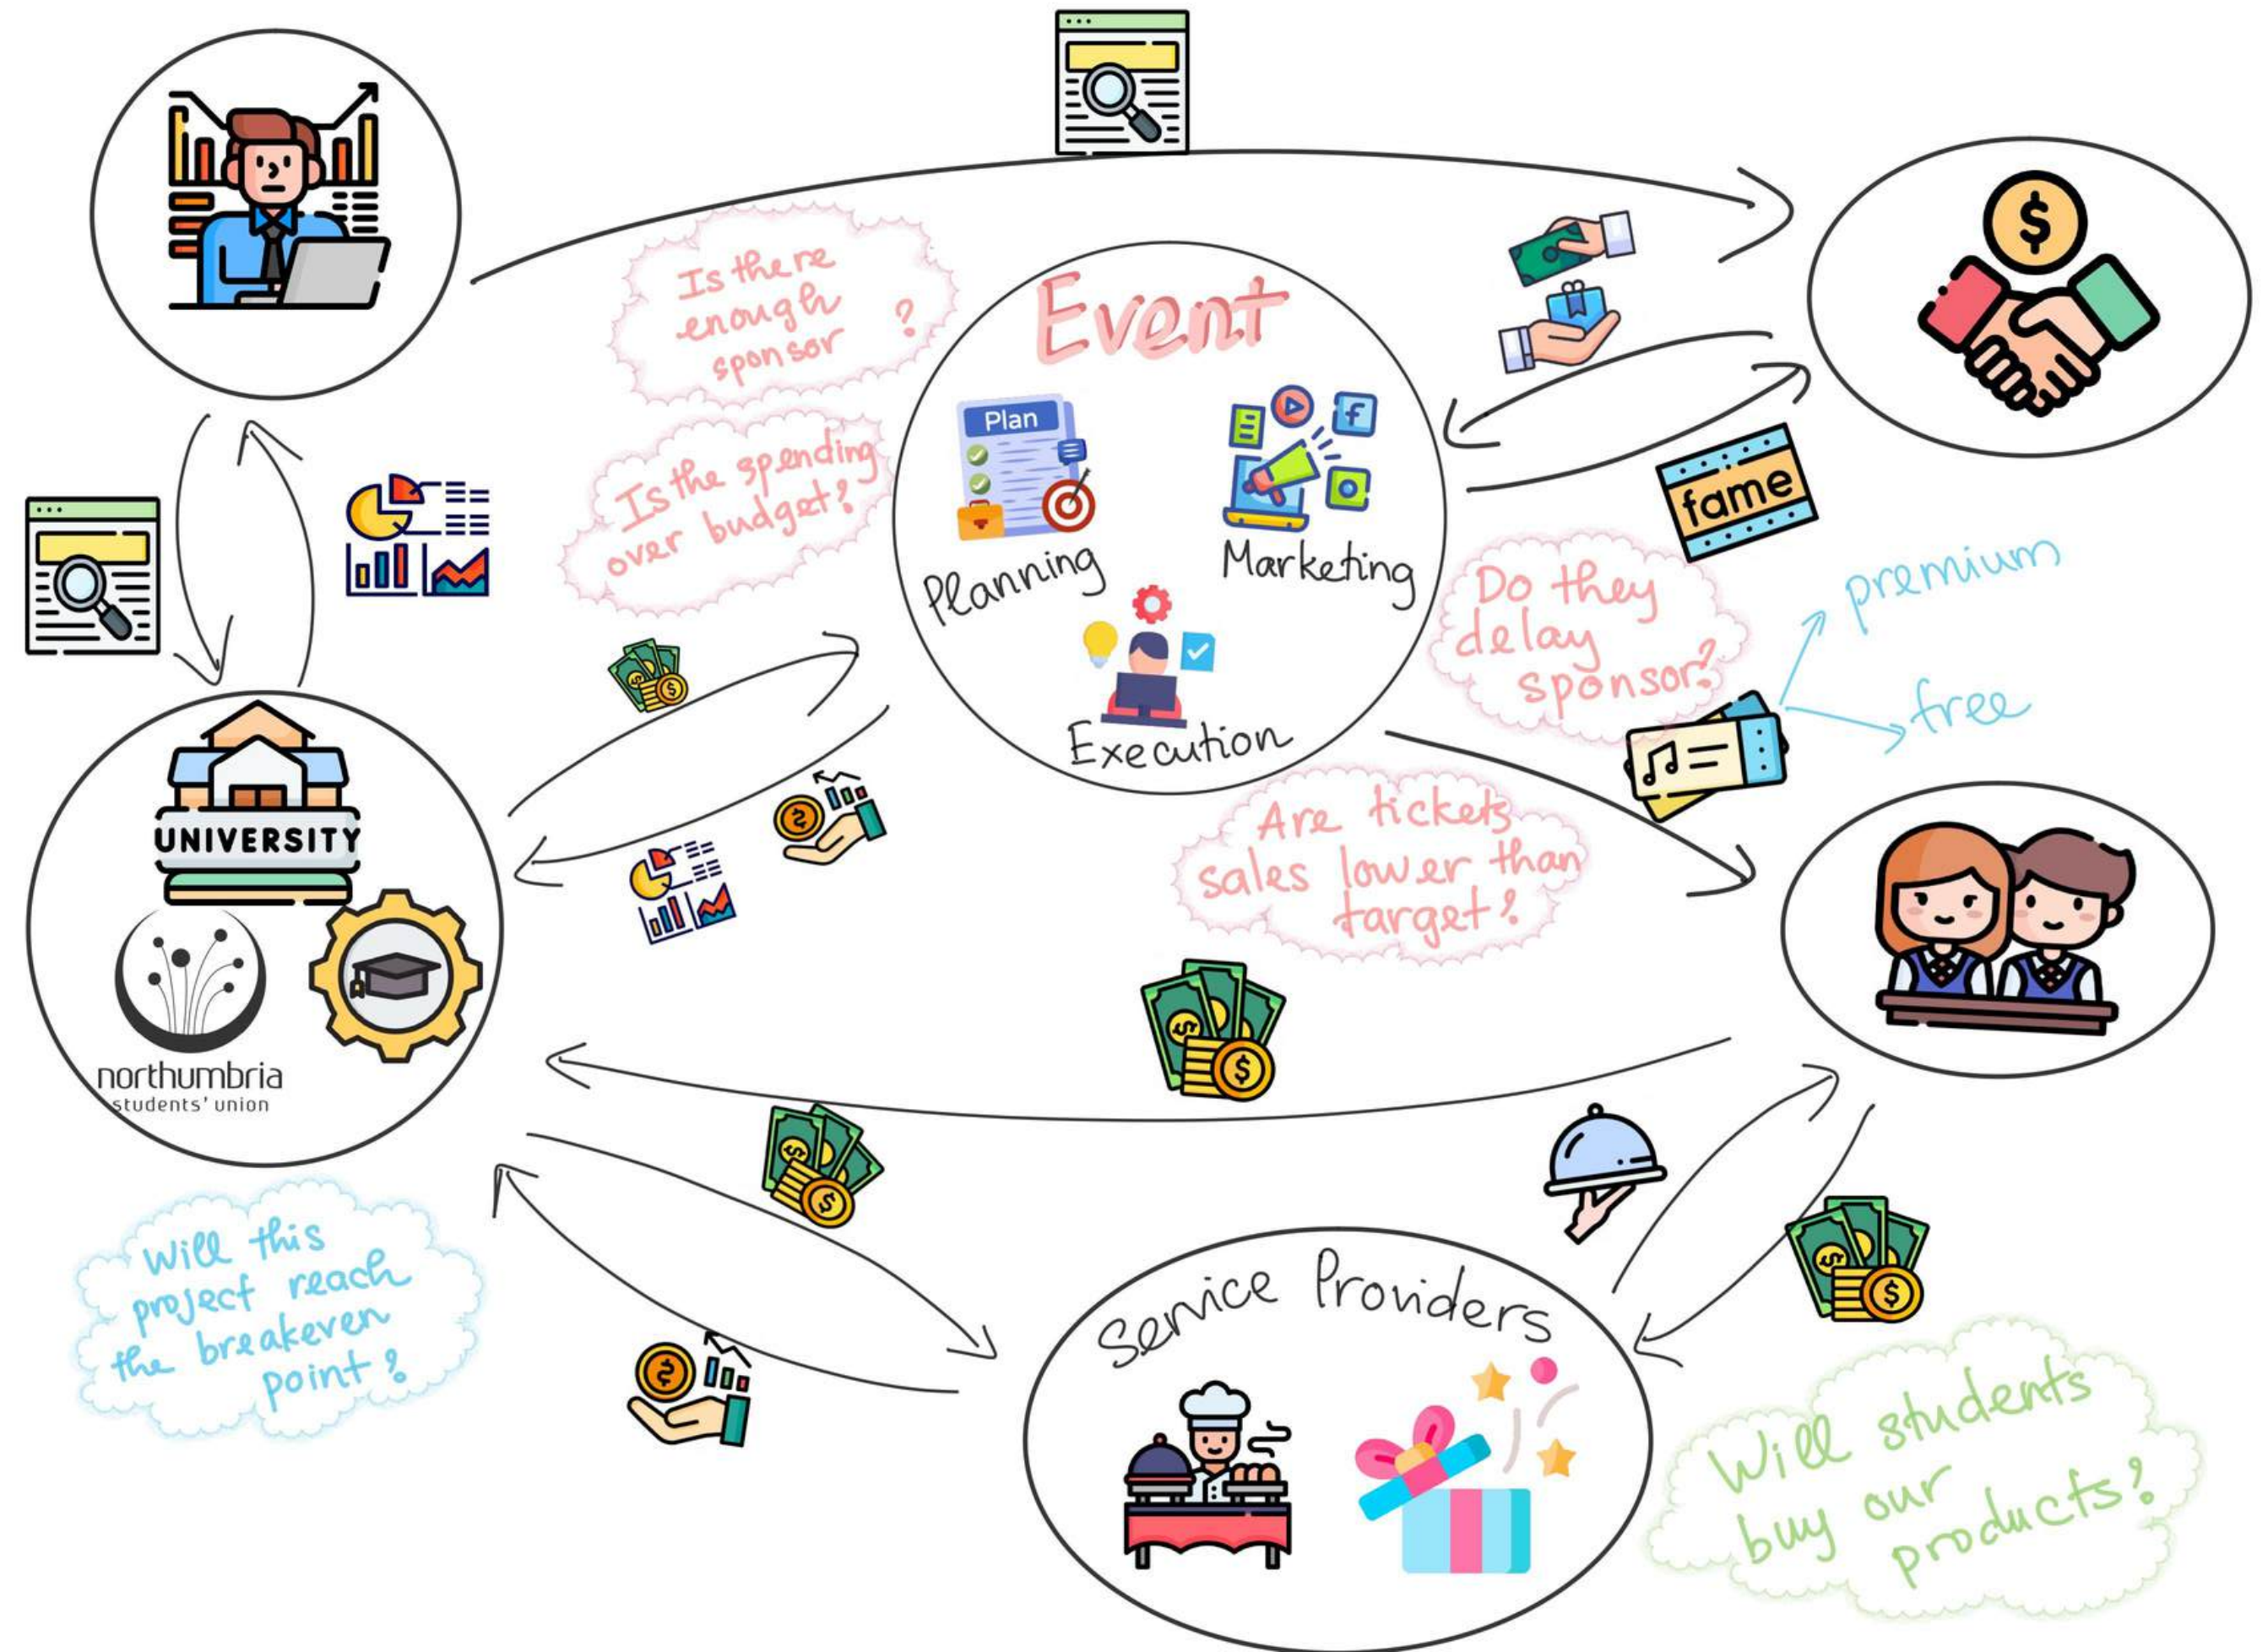

CATWOEE ANALYSIS

CUSTOMER

- Students, guests
- University
- Sponsors
- Service providers



ACTORS

- Event team
- Student Union Management
- Service providers (F&B, merchandise)
- Analyst team



TRANSFORMATION

Converting an initial unstructured event idea into a fully planned, funded, coordinated, and executed event that delivers value to students and brand exposure to sponsors



WORLVIEW

- A collaborative value-creation ecosystem where students, sponsors, and the university all benefit.
- Enhancing student experience, campus culture, and sponsor reputation



OWNER

- University
- Sponsors




ENVIRONMENTAL CONSTRAINTS

- University policies
- Budget limitations
- Time & academic schedules
- Sponsor expectations
- Safety requirements and risk management protocols



STAKE- HOLDERS

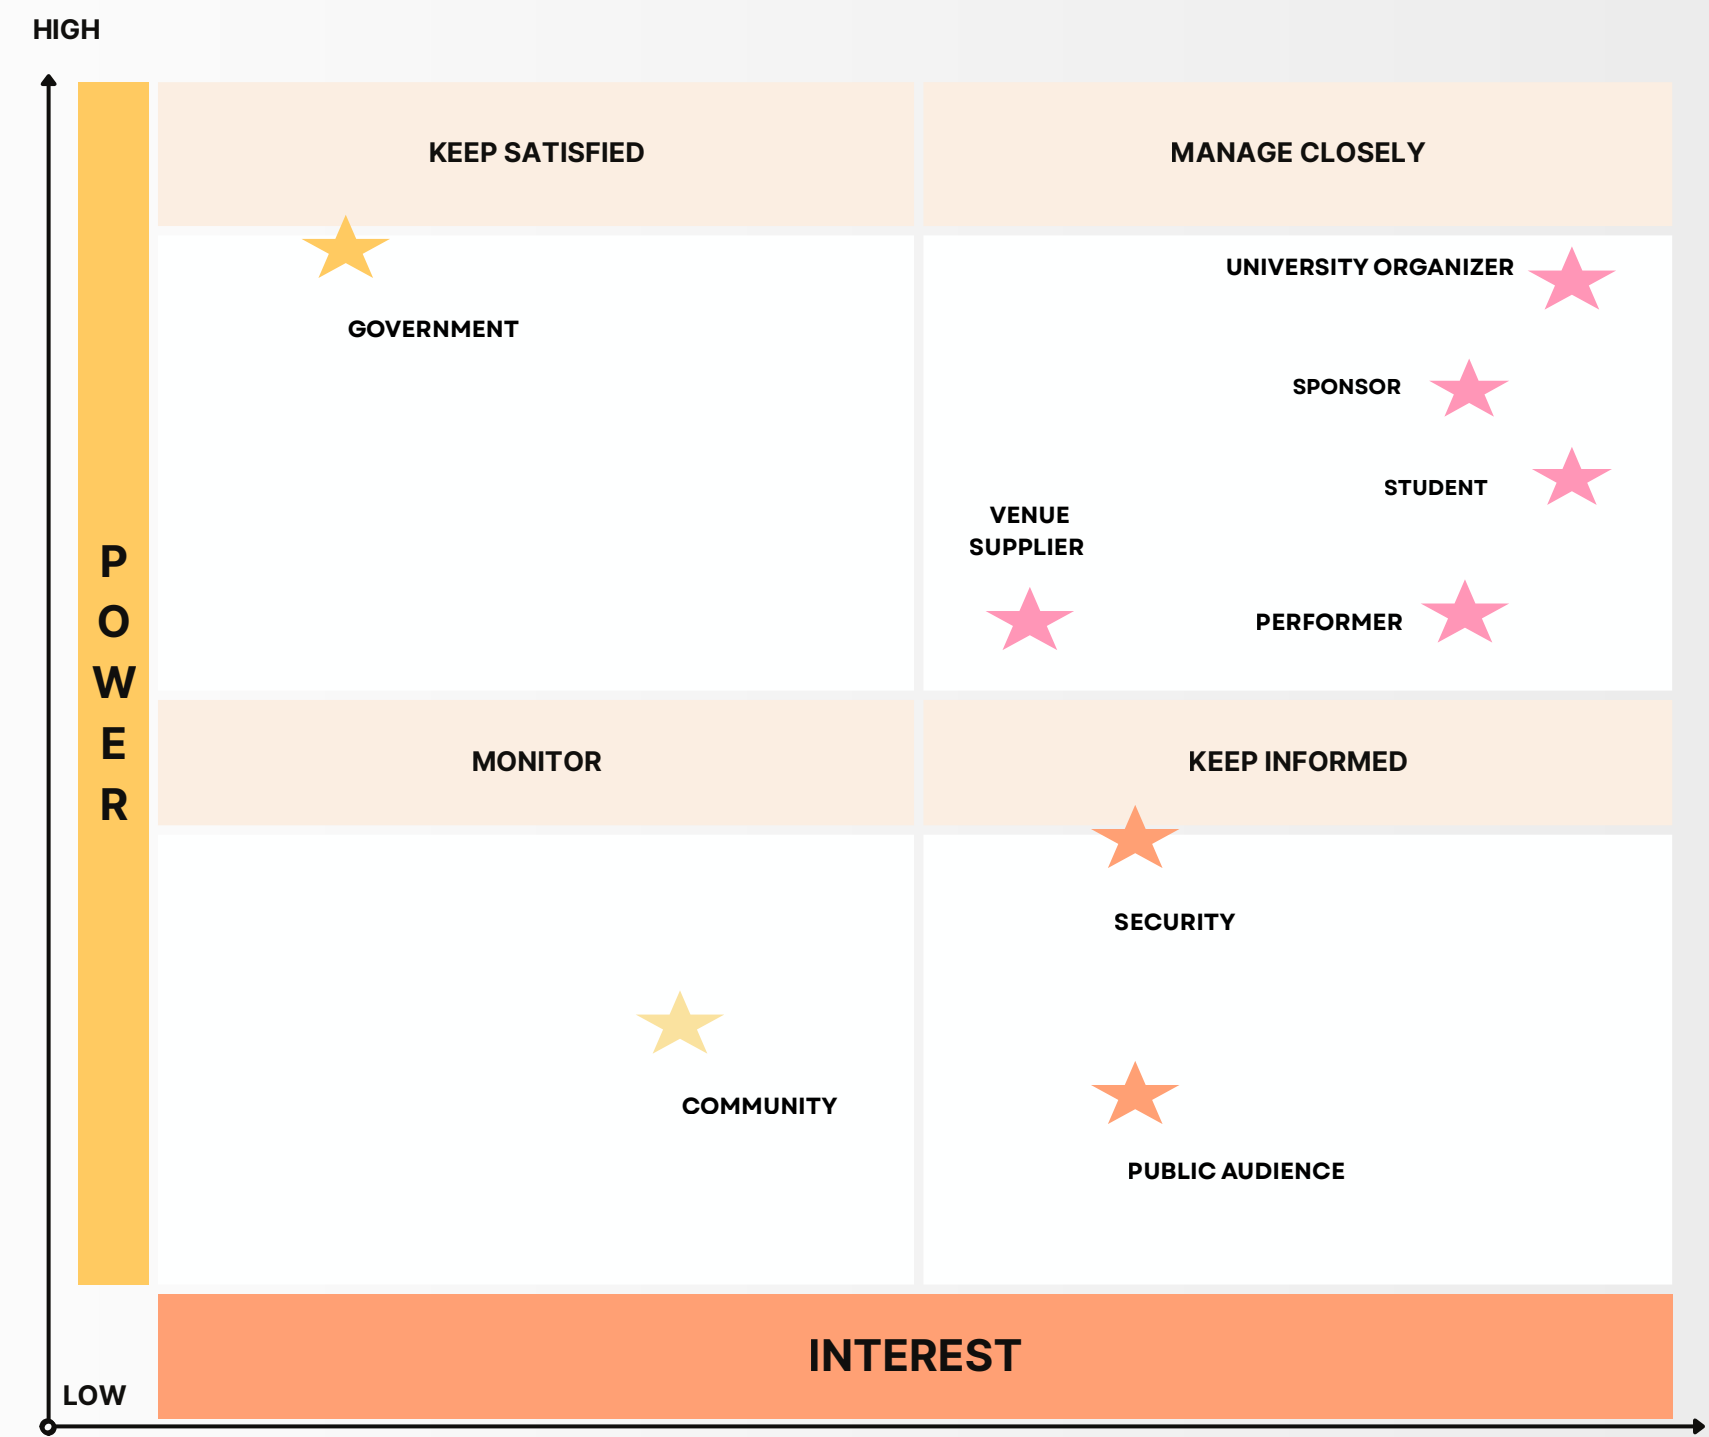

Stakeholder Map			
	Stakeholder Name	Level of Power	Level of Interest
1	University organizer	10	9
2	Students	7	9
3	Sponsor	8	8
4	Performancer	6	8
5	Venue supplier	6	6
6	Public audience	4	7
7	Security	5	7
8	Government	10	2
9	Community	3	4

GANNT CHART


Project Start:	Mon, 10/11/2025
----------------	-----------------

Mon, 10/11/2025


					10 Nov 2025							17 Nov 2025							24 Nov 2025							1 Dec 2025							8 Dec 2025							15 Dec 2025							22 Dec 2025							29 Dec 202																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
					10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
TASK	ASSIGNED TO	PROGRESS	START	END	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Sprint 1 Discussing																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

UNIVERSITY ORGANIZER


Tickets sales by channel

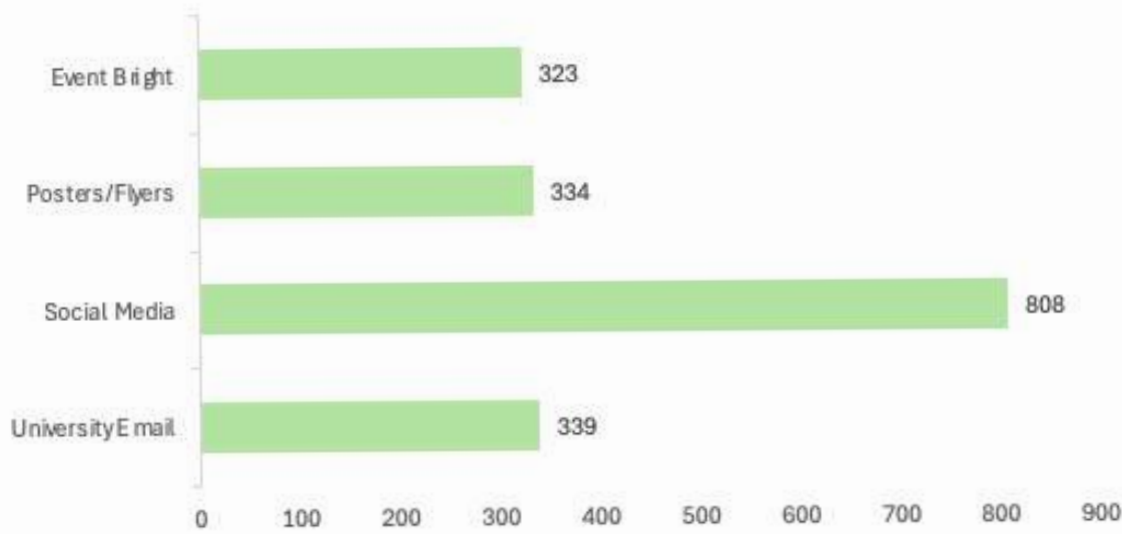


Total cost by category

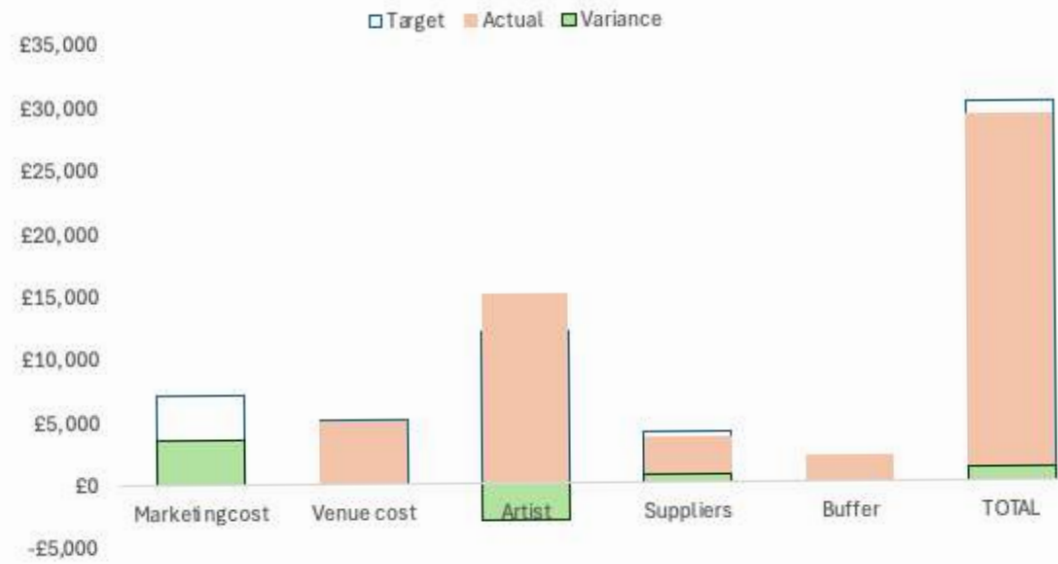

Target vs Actual sales by Week

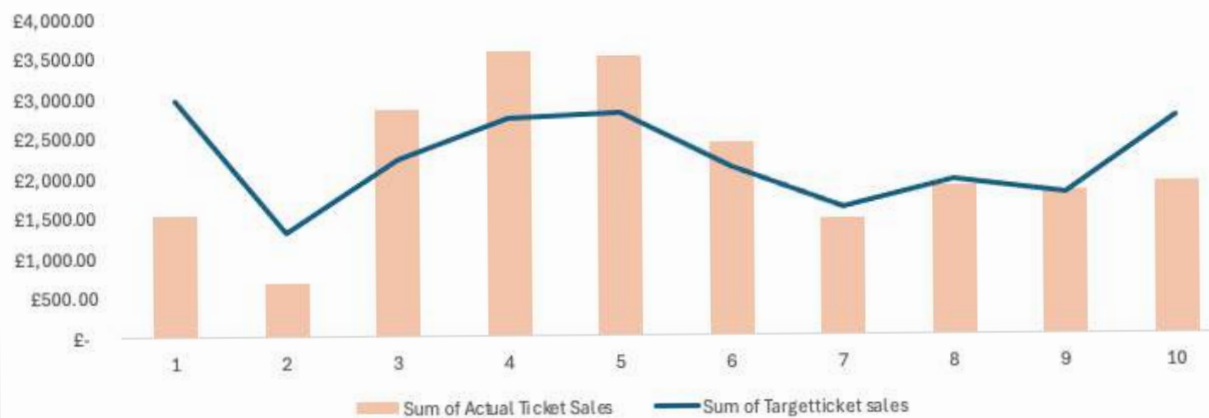


Concert Attendees

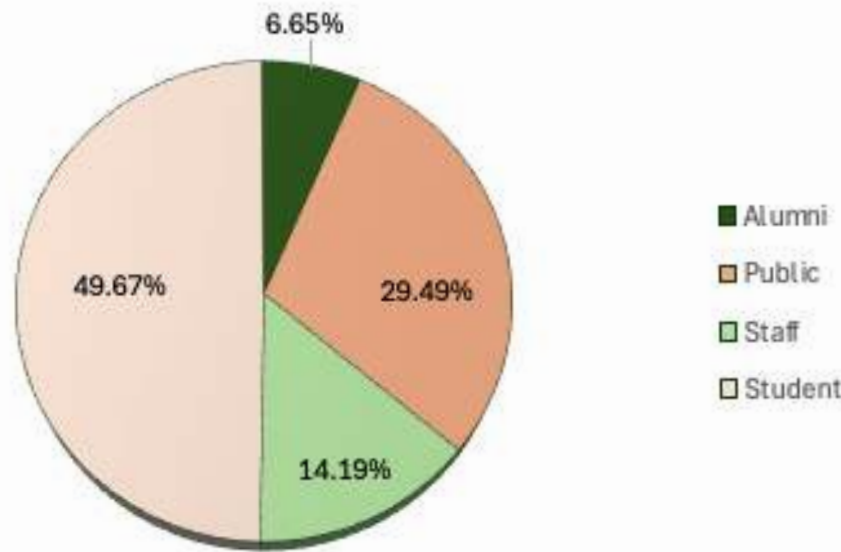


PERFORMANCER/ARTIST

% Promotion Type

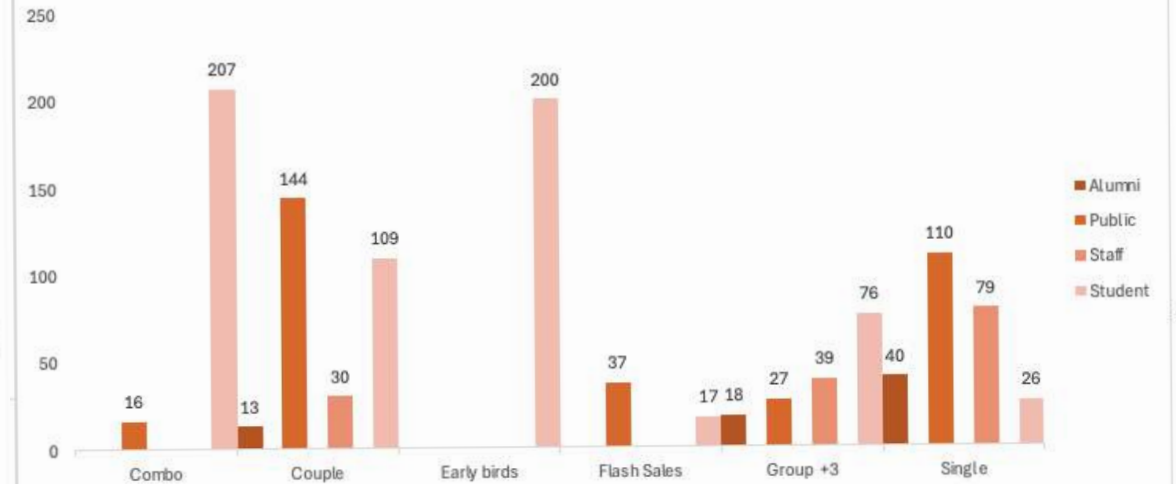


% CPI

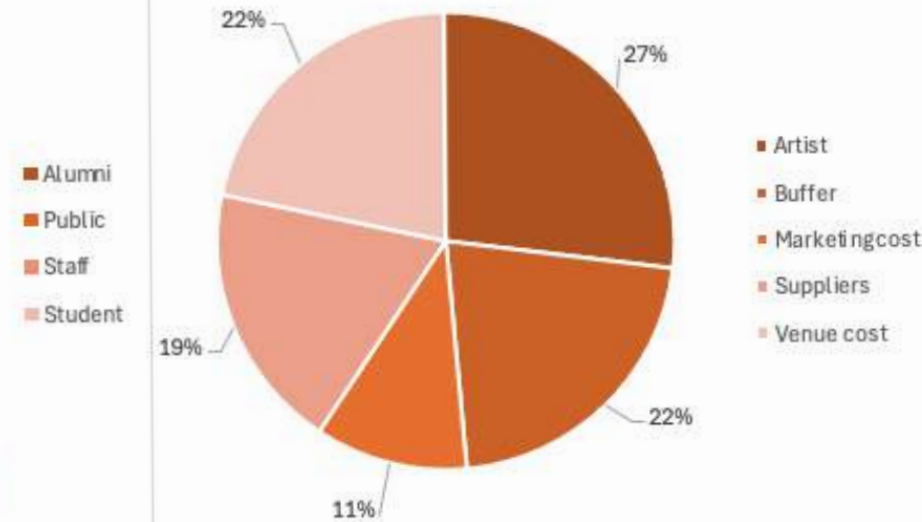


SPONSOR

Funding

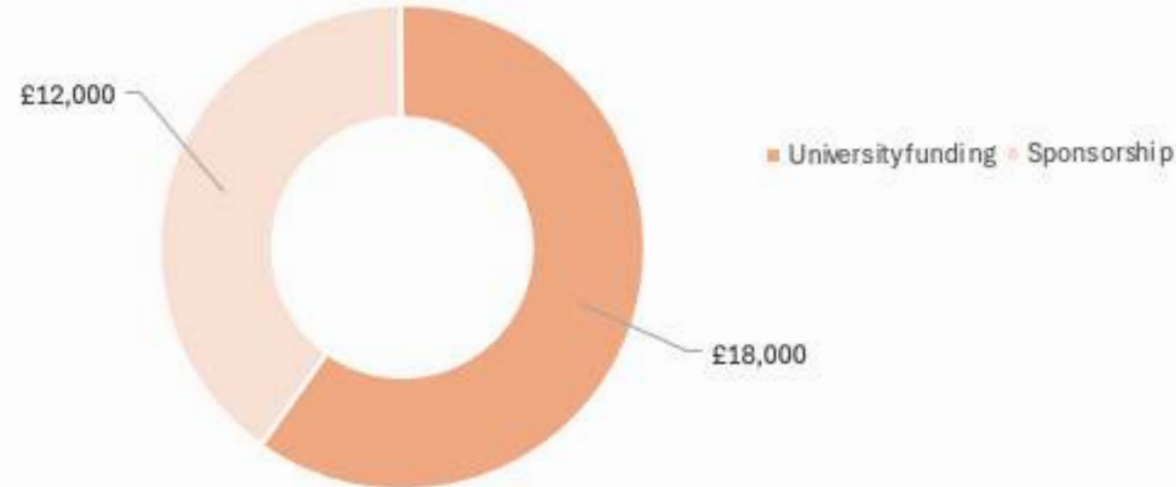

% Evolution Sales Per Stage

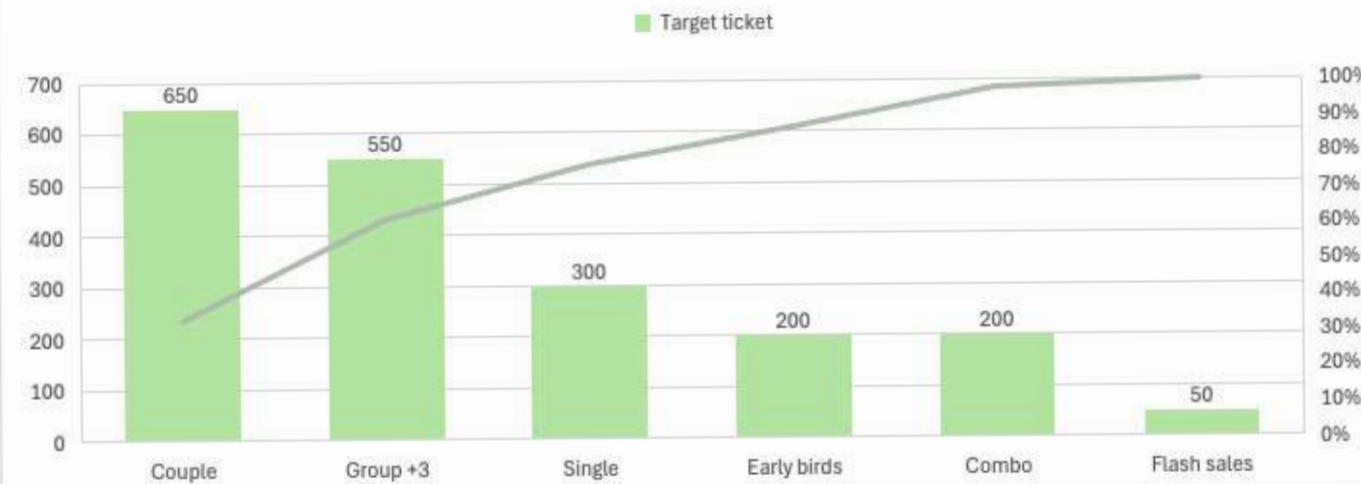


Promotion Type


- Combo
- Couple
- Early birds
- Flash Sales
- Group +3
- Single

SPI & CPI

Phase	Planed time	Actual time	Planned Value	Earned Value	Actual Cost	SPI	CPI
Planning	15	15	£3,600	£3,500	£3,400	972	1,029
Venue	25	25	£6,000	£5,700	£5,800	950	983
Marketing	20	20	£5,500	£5,600	£5,000	1,018	1,120
Ticketing & Customer Service	10	9	£2,700	£2,500	£2,600	926	962
Security	18	17	£5,000	£4,700	£4,900	940	959
Technical Setup	8	10	£2,400	£2,300	£2,500	958	920
Rehearsals	8	8	£2,800	£2,700	£2,900	964	931
Concert	6	6	£2,000	£1,900	£2,300	950	826
TOTAL	110	110	£30,000	£28,900	£29,000	963	997

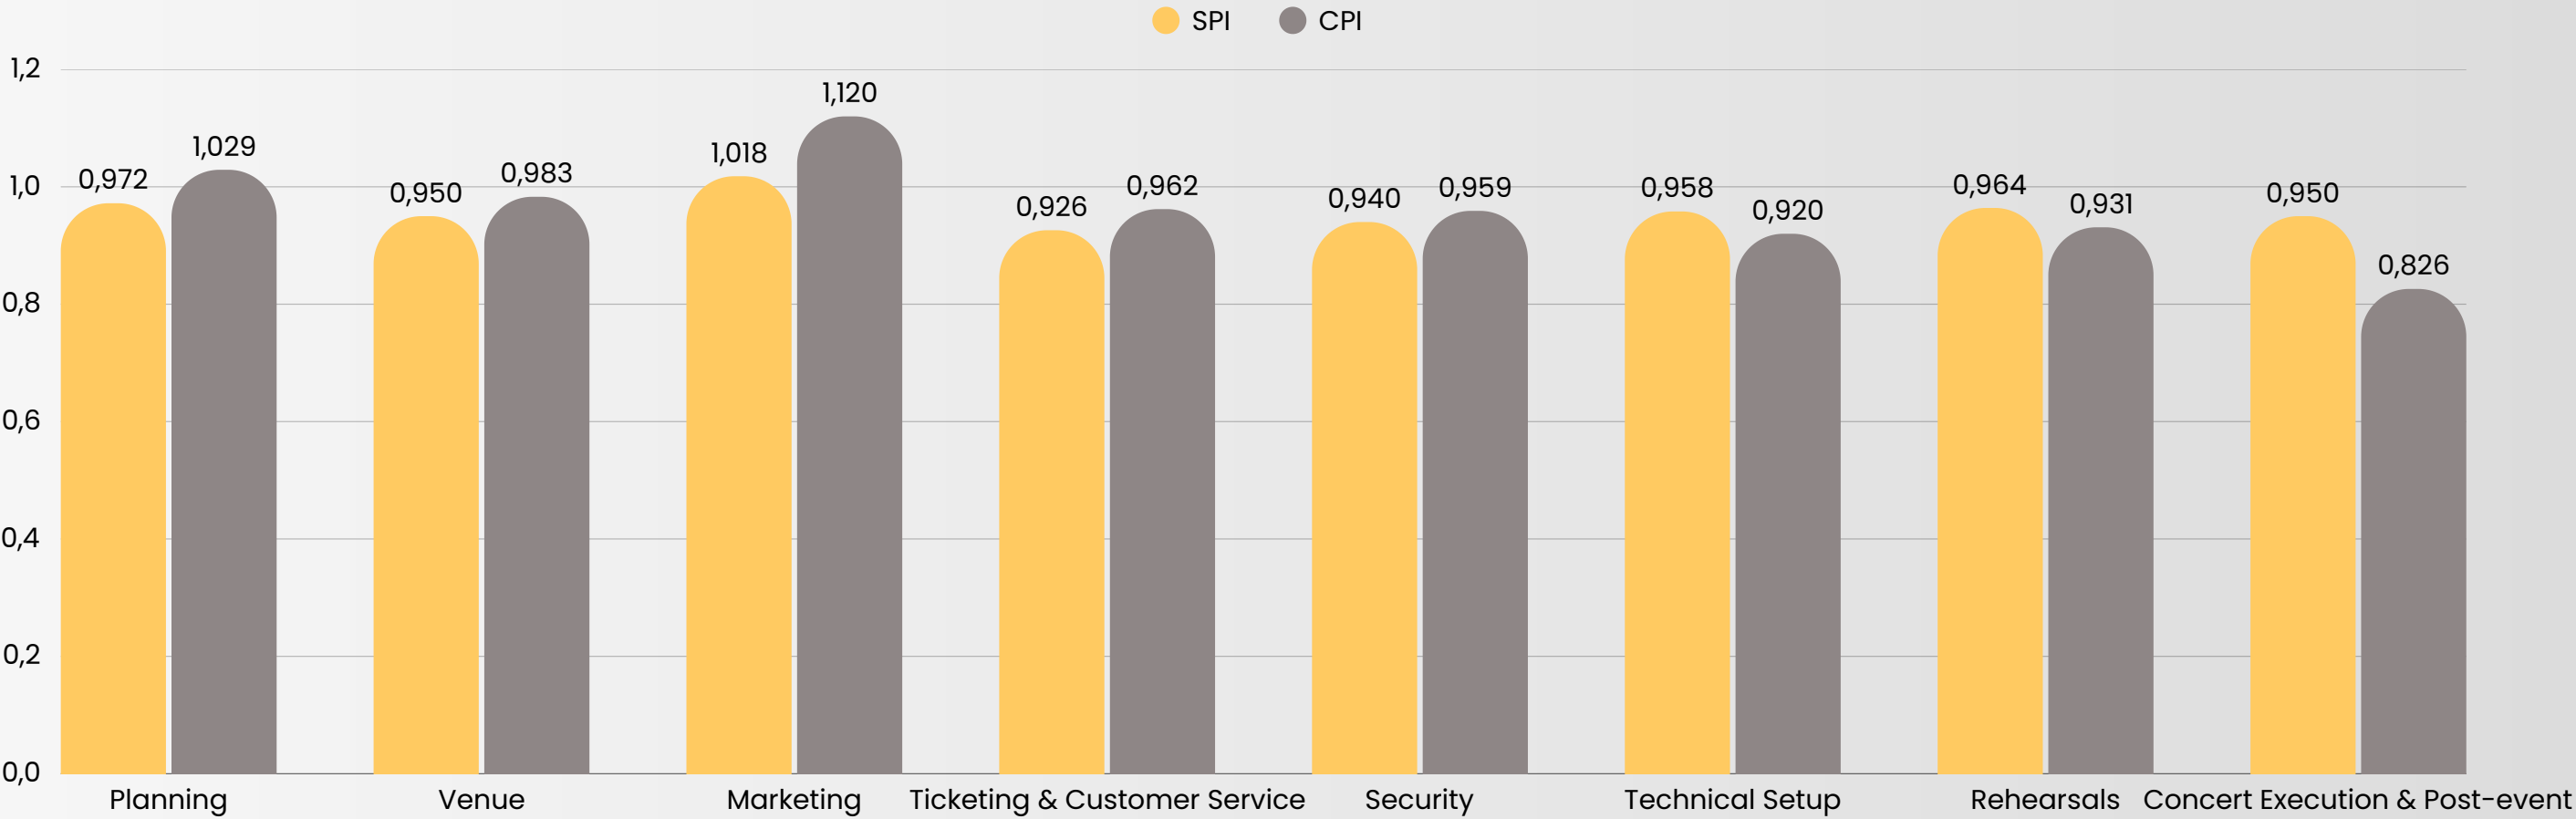

SPI/CPI ANALYSIS

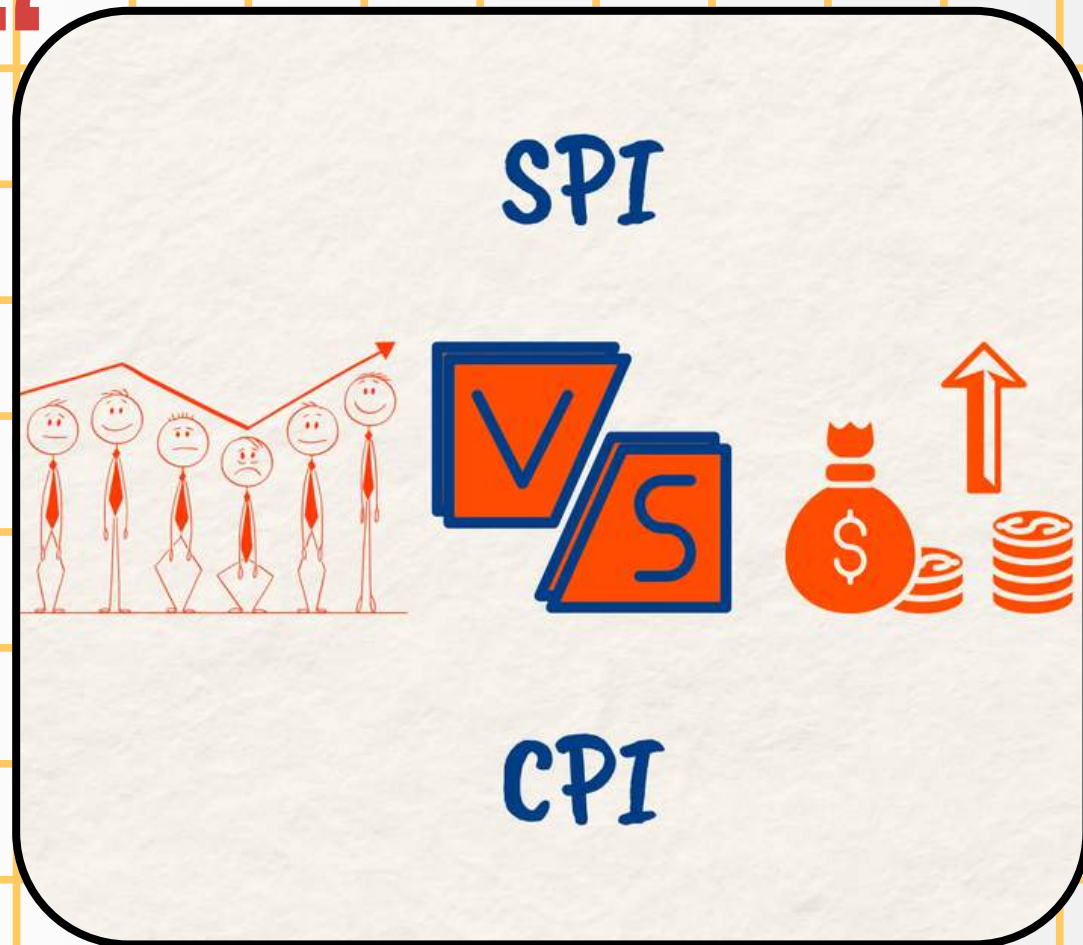

Schedule Performance Index (SPI): 0.963 (<1)

The project is slightly behind schedule, completing approximately 96.3% of the planned work.

Cost Performance Index (CPI): 0.997 (<1)

Cost performance is nearly on budget, with only a 0.3% variance.

Summary:

- Time: 110 planned days
- Earned Value (EV): £28,900

Compared to:

- Planned Value (PV): £30,000
- Actual Cost (AC): £29,000



The slight gap between EV and PV explains the minor schedule delay and near-perfect cost alignment.

Risk ID	Risk Name	Risk Description	Probability	Impact	Risk Owner	Risk level	Mitigation strategies	Status	Note/ Immediate Action
1	Difficulty attracting investment capital	The sponsor may withdraw from project in last minutes, or lack funding.	Likely	Major	Project Manager	Very High	Signed a clear sponsorship contract with a penalty payment.	Open - mitigated	Received: 100/100%
									HEYTEA: £6,000
									EAT VIET: £6,000
									QA Higher Education: £18,000
									COMPLETED
2	Cost over-run	including those that may arise due to unexpected performers or artists and HR fees.	Possible	Moderate	Financial Manager	High	- Weekly expense tracking reports - Locked the supplier price.	Open - controlled	28/11: Send final quotes back to all suppliers; request that they hold prices until 12/31.
									COMPLETED
3	Cancellation or delay	The concert may delay or get cancelled due to technological issue, security problems, and overcrowding.	Possible	Severe	Operational Director	Very High	- Buy event insurance. - Technical excess & backup systems. - Crowd management & capacity control plan.	Open-mitigated	Request to buy immediately
									<u>Hiscox UK</u> / CAUNCEO HARA
									COMPLETED
									Event day: 3 entry queues + wristband system
									Refund policy
4	Lower ticket sales	Getting lower than expected because of student availability and poor promotions.	Likely	Major	Marketing Director	Very High	- Additional TikTok and Instagram budget promotion. - Flash sale, combos promotion	Open	Daily meeting for any adjustments and sale dashboard.
5	Poor cashflow management	Errors occur, resulting in penalties due to improper management of expense payments, etc.	Likely	Major	Finance Manager	Very High	- Cash flow forecast, weekly, and payment calendar. - Centralised payment trackers (Xero, Google Sheet).	Open - mitigated	Bank reconciliation every Monday
									Monitoring penalty clause



RECOMMENDATION

UNIVERSITY ORGANIZER

- Approve and prioritize **the 50% off flash sale and combo promotion.**
- Surplus **Ticket and Gift Giveaway for volunteers.**
- Develop **a success report** after the event.

SPONSOR

- Integrate **sponsor brands** into Flash Combo
- Provide UGC data to sponsors.
- Propose **a Long-Term Partner Relationship contract.**

STUDENT

- Approve communication plan and allocate **the marketing budget.**
- Use **Volunteer UGC** to increase appeal for student audience
- Highlight **limited-time benefits** to encourage student purchasing early.

PERFORMANCER

- Invite performers to participate in the flash sale promotion **across their channels.**
- Coordinate **Technical Adjustments**




CONCLUSION



Financial Target

- Implementing financial management, weekly real sales tracking, and data-driven flash sales and combos in 72 hours
 - resulting in sufficient revenue to reach the full breakeven target (98% seat occupancy).



Operational & Artistic Target

- Secured all performers and venue suppliers with fixed-cost contracts, and technological rehearsal was completed.
- Developed the backup plan
- Ensures the event operates fluently and mitigates high risks.



Stakeholder Satification Target

- University organizers are managed closely, receiving weekly dashboards and reports.
- Sponsors respond supportively with punctual funding.
- Positive reaction of students to pricing and promotion.



REFERENCE



Kerzner, H. (2017). Project management: A systems approach to planning, scheduling, and controlling (12th ed.). John Wiley & Sons.

Norman, M. (2025). Everything you need to know about concert planning: A comprehensive guide for success. Eventunity. <https://eventunitypro.com/everything-you-need-to-know-about-concert-planning/>


Bell, S., & Morse, S. (2013). How people use rich pictures to help them think and act. Systemic Practice and Action Research, 26(4), 331–348. <https://doi.org/10.1007/s11213-012-9236-x>

Alboud, M., Recker, J., & Indulska, M. (2025). Conceptual modeling: Foundations, a historical perspective, and a vision for the future. Data & Knowledge Engineering. <https://doi.org/10.1016/j.datak.2025.102483>

Oakinterlink. (2025). 10 common project problems and how to solve them like a pro. <https://oakinterlink.com/10-common-project-problems-and-how-to-solve-them-like-a-pro/>

Project Management Institute. (2021). A guide to the project management body of knowledge (PMBOK® guide) (7th ed.). Project Management Institute

MATERIALS

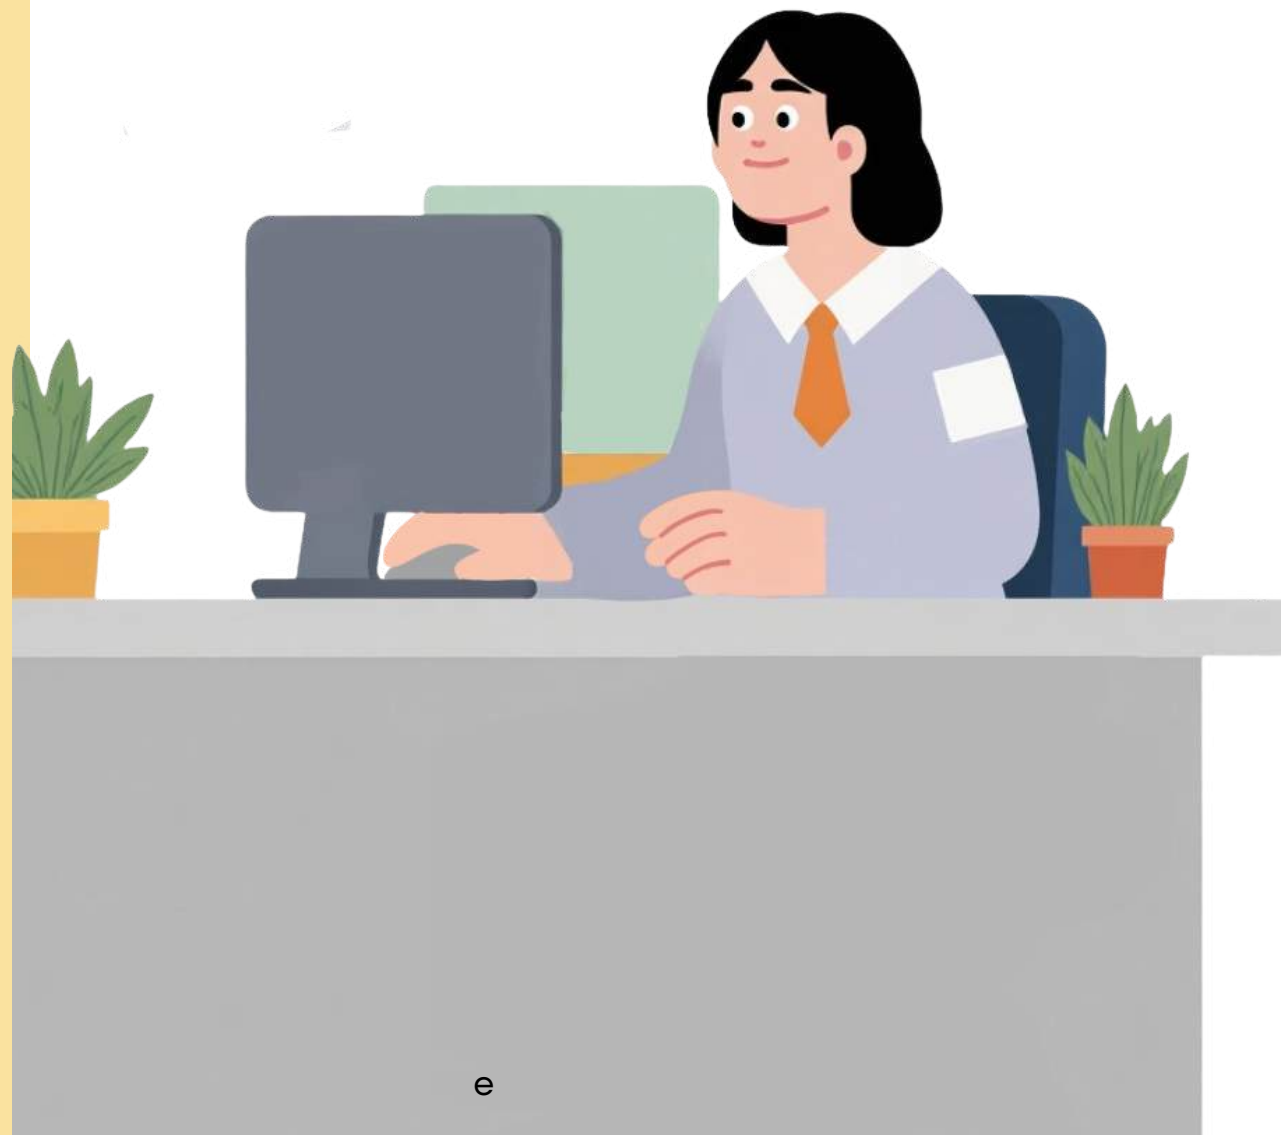

Trello

[https://trello.com/b/ATgp8tJ1/concert-evaluation-project?
utm_source=eval-email&utm_medium=email&utm_campaign=board-
invite](https://trello.com/b/ATgp8tJ1/concert-evaluation-project?utm_source=eval-email&utm_medium=email&utm_campaign=board-invite)



Data-dashboard Excel

[https://livenorthumbriaac-
my.sharepoint.com/:x/g/personal/w25045434_northumbria_ac_uk/IQDo
jYmnKoovQ7XG7kKVjDeKAe_ykvqgQUv5gt-QvI26kl8?e=98fBoC](https://livenorthumbriaac-my.sharepoint.com/:x/g/personal/w25045434_northumbria_ac_uk/IQDojYmnKoovQ7XG7kKVjDeKAe_ykvqgQUv5gt-QvI26kl8?e=98fBoC)



Gannt-chart

[https://livenorthumbriaac-
my.sharepoint.com/:x/g/personal/w25045434_northumbria_ac_uk/IQCc
gn1xCnltQZhflh_B1_hTAS2cIshPnV83DlnUpRuiXZY?e=kFCdHW](https://livenorthumbriaac-my.sharepoint.com/:x/g/personal/w25045434_northumbria_ac_uk/IQCcgn1xCnltQZhflh_B1_hTAS2cIshPnV83DlnUpRuiXZY?e=kFCdHW)

Thank You

